


PHASE 1 TO 3 - TREE PRUNING/FELLING AND ERECTION OF TREE PROTECTION FENCING




CONSTRUCTION PHASE

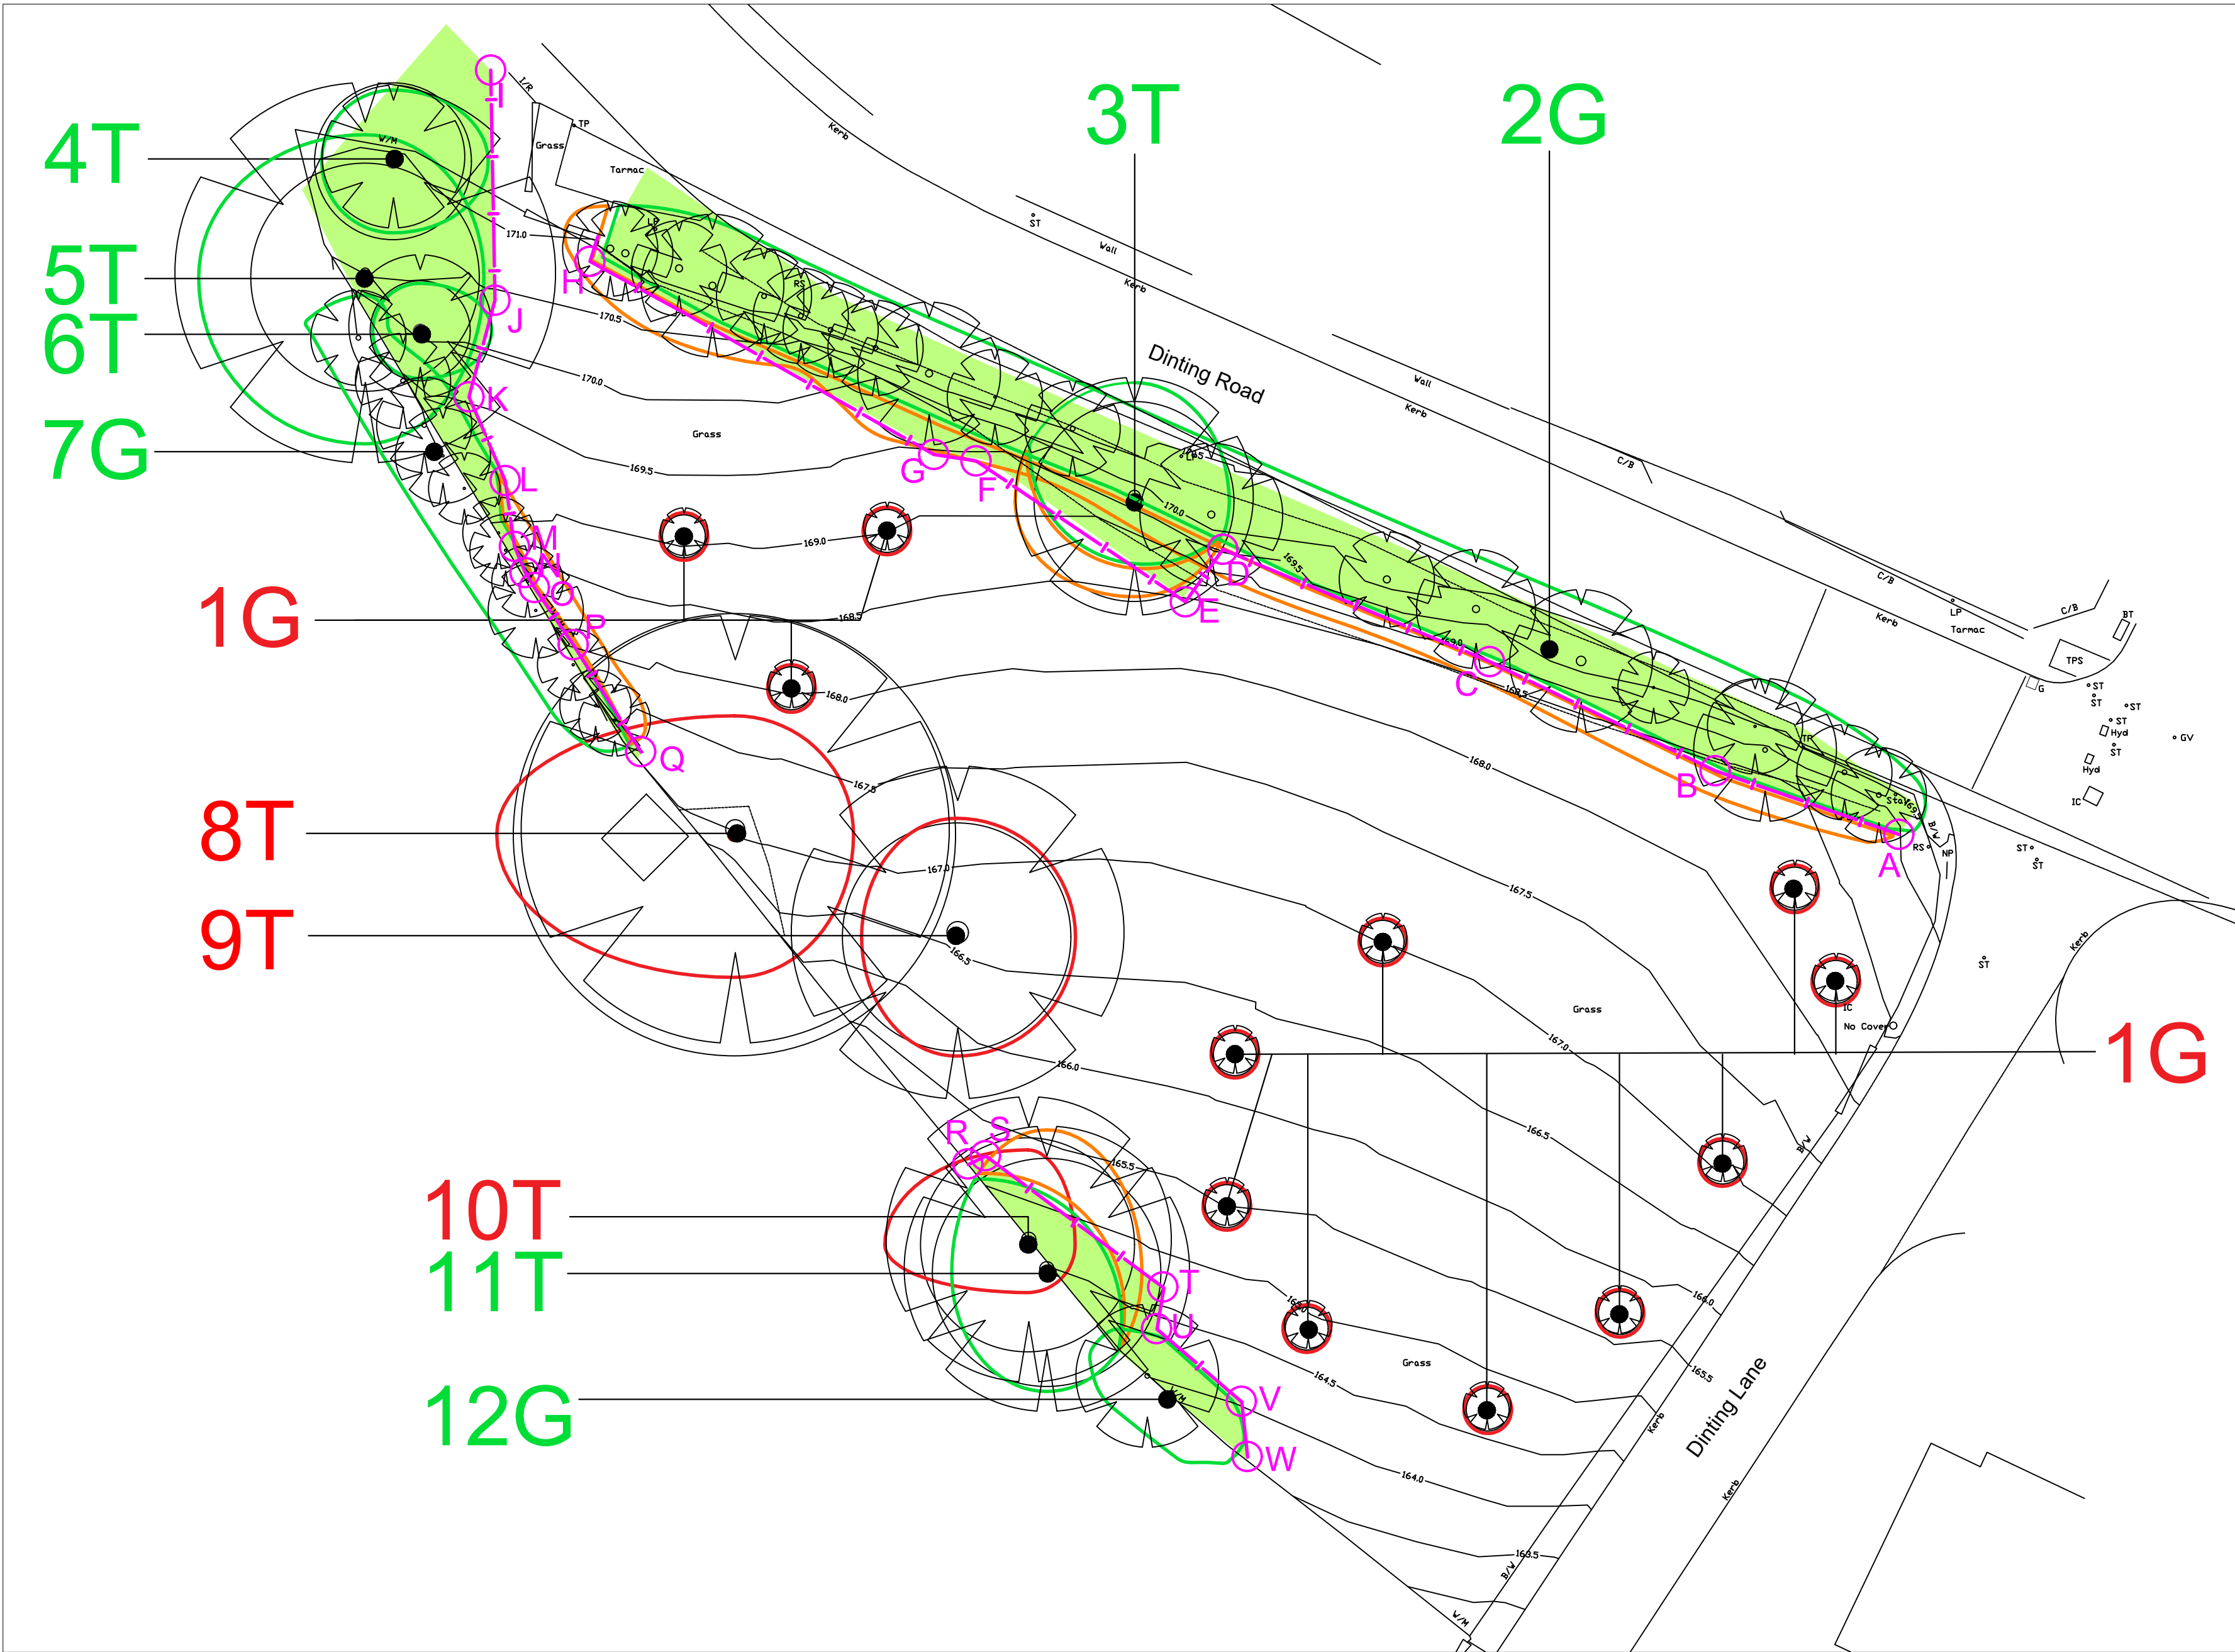

Tree Schedule			
Tree Number	Species	RPA Radius	Category
1G	Mixed Species New Planting	0.9m	C3
2G	Lapsed Hawthorn Hedging		C1
3T	Sycamore	4.2m	C1
4T	Hawthorn	3.3m	C1
5T	Ash	4.8m	C2
6T	Common Oak	2.1m	C1
7G	Row of Lawson Cypress		C2
8T	Sycamore	9.3m	U
9T	Sycamore	4.8m	C1
10T	Goat Willow	4.5m	U
11T	Goat Willow	4.8m	C2
12G	4x Silver Birch		C2


EASTING & NORTHING POINTS FOR FULL SPEC.		
A	402371.37	394568.26
B	402363.65	394570.93
C	402354.16	394575.52
D	402342.94	394580.24
E	402341.37	394578.03
F	402332.56	394583.96
G	402330.78	394584.23
H	402316.32	394592.34
I	402312.15	394600.39
J	402312.33	394590.72
K	402311.23	394586.65
L	402312.76	394583.13
M	402313.15	394580.36
N	402313.6	394579.26
O	402313.98	394578.65
P	402315.62	394576.23
Q	402318.46	394571.74
R	402332.22	394554.37
S	402332.98	394554.73
T	402340.46	394549.18
U	402340.17	394547.45
V	402343.74	394544.39
W	402343.98	394542.08

Phase	Requirements	Method																				
1 Prior to erection of protective fencing.	Undertake tree and vegetation removal and pruning works Trees/vegetation to be removed:  Trees/vegetation to be pruned: 	Refer to section 5.5 of AIA/MS report. All tree works to be carried out to BS3998: 2010: by suitably qualified and insured professional tree surgeons. The following tree felling must be undertaken at this Phase: <table><tr><th colspan="2">Items requiring removal:</th></tr><tr><td>1G</td><td>Mixed Species New Planting</td></tr><tr><td>8T</td><td>Sycamore</td></tr><tr><td>9T</td><td>Sycamore</td></tr><tr><td>10T</td><td>Goat Willow</td></tr></table> The following tree pruning must be undertaken at this Phase: <table><tr><th colspan="2">Items requiring pruning:</th></tr><tr><td>2G</td><td>Lapsed Hawthorn Hedge. Prune back the southerly lateral canopy spread by some 1.2m from the hedge extremities.</td></tr><tr><td>3T</td><td>Sycamore. The southerly (side side) lateral canopy spread requires reducing by approximately 1.5m in length to facilitate clearance for construction</td></tr><tr><td>7G</td><td>Lawson Cypress Row. Prune back a section of the row back to the boundary (refer to drawing).</td></tr><tr><td>11T</td><td>Goat Willow. Reduce the northerly lateral canopy of the tree by approximately 2.5m in length to provide some clearance of the adjacent proposed garden area.</td></tr></table>	Items requiring removal:		1G	Mixed Species New Planting	8T	Sycamore	9T	Sycamore	10T	Goat Willow	Items requiring pruning:		2G	Lapsed Hawthorn Hedge. Prune back the southerly lateral canopy spread by some 1.2m from the hedge extremities.	3T	Sycamore. The southerly (side side) lateral canopy spread requires reducing by approximately 1.5m in length to facilitate clearance for construction	7G	Lawson Cypress Row. Prune back a section of the row back to the boundary (refer to drawing).	11T	Goat Willow. Reduce the northerly lateral canopy of the tree by approximately 2.5m in length to provide some clearance of the adjacent proposed garden area.
Items requiring removal:																						
1G	Mixed Species New Planting																					
8T	Sycamore																					
9T	Sycamore																					
10T	Goat Willow																					
Items requiring pruning:																						
2G	Lapsed Hawthorn Hedge. Prune back the southerly lateral canopy spread by some 1.2m from the hedge extremities.																					
3T	Sycamore. The southerly (side side) lateral canopy spread requires reducing by approximately 1.5m in length to facilitate clearance for construction																					
7G	Lawson Cypress Row. Prune back a section of the row back to the boundary (refer to drawing).																					
11T	Goat Willow. Reduce the northerly lateral canopy of the tree by approximately 2.5m in length to provide some clearance of the adjacent proposed garden area.																					
2 Prior to any construction works on site	Erection of protective fencing: To retain throughout the duration of the development. 	Protective fencing is to be erected in accordance with 5.6 of AIA/MS report. The fencing must comply with the positions shown in the Tree Protection Plan. Fencing 'node' positions are to be marked using supplied co-ordinates and a scaffold brace fence created. No works, no storage of materials, no access, or any ground disturbance is to take place within the Tree Protection Barrier Fencing other than works specified within the Arboricultural Method Statement. Fenced areas are to be treated as Construction Exclusion Zones. Warning signs to be placed on all protective fencing. For large sections of fencing the signs must be placed at 20m intervals. Signs must be laminated and securely attached at all corners. Two signs are to be placed side by side; copies of which are attached within Appendix A.																				
3 Verifying quality of protective barriers	Verify that the location and quality of tree protection barriers is adequate prior to onset of main site works.	Site visit with Arboricultural Consultant and Site Manager. Tree Officer to be pre-informed of visit. In order for set works to proceed the pro-forma in Appendix B of the AIA/AMS report is to be completed and passed on to the local planning authority: If the protective barriers are not adequately, work is not to proceed until rectified.																				

Phase	Requirements	Method
4	Completion of main construction and undertaking of landscaping	Landscaping and dismantling of tree barrier protective fencing. It is essential that ground levels within the root protection areas are not altered, either by raising or lowering soil levels; even at the landscaping stage. Landscaping operations must be undertaken in a manner that will not impact trees. Landscaping within the root protection area of trees must be undertaken in the following manner: - Any existing ground flora (grass/weeds/scrub) is to be sprayed with a systemic herbicide and left to die-off, or skimmed off using hand tools. - Dead flora is to be trimmed as hard as possible with a brush cutter or similar. The bulk of the trimmed material is to be removed by raking. - A good quality organic topsoil layer may be placed down. Small depressions may be filled (and lightly compacted underfoot). Placed topsoil soil layers must not exceed 100mm depth. - No plant machinery operating within the root protection areas to exceed 1 tonne gross weight and must only operate from propriety ground protection boards such as DuraMatt Access Mats (see Appendix C). - Turf and other planting to proceed thereafter.
5	Completion of construction and installation of boundary treatments	Within the Construction Exclusion Zones of retained trees the wooden fencing shall be installed as follows. - Hand tools only - Exploratory post holes to be dug. Any roots encountered less than 2.5cm diameter should be cleanly cut back. - Roots in excess of 2.5cm can only be removed once arboricultural advice has been sought. - Where roots in excess of 8cm are encountered, an alternative location for the post hole is required. - Prior to the pouring of concrete a non-permeable membrane must fully line the post hole.

THIS DRAWING MUST BE VIEWED
IN COLOUR AND READ IN
CONJUNCTION WITH
ARBORICULTURAL IMPACT
ASSESSMENT AND METHOD
STATEMENT

SCALE - 1:200



LPA Comments Added Scale Bar

01.11.23	HS	B
Amends to layout	29.09.23	MG A
© Copyright reserved	Date	Drawn

Landscape Architecture
Arboriculture

Trevor Bridge Associates Ltd
Ashdon Old Batts
Stanford Street West
Ashdon-under-Lyne
Lancs OL6 7FW

Tel: 0161-804 2099
E-mail: info@trevorbridge.co.uk

Project
Land off Dinting Road/Dinting Lane,
Glossop, SK13 7DY
Aspire Homes

Title
Tree Protection Plan

Date Dec '21	Scale(s) 1:200 @ A0	Dwg no 6804.02	Rev A
Dwn MG	Chk'd		
