
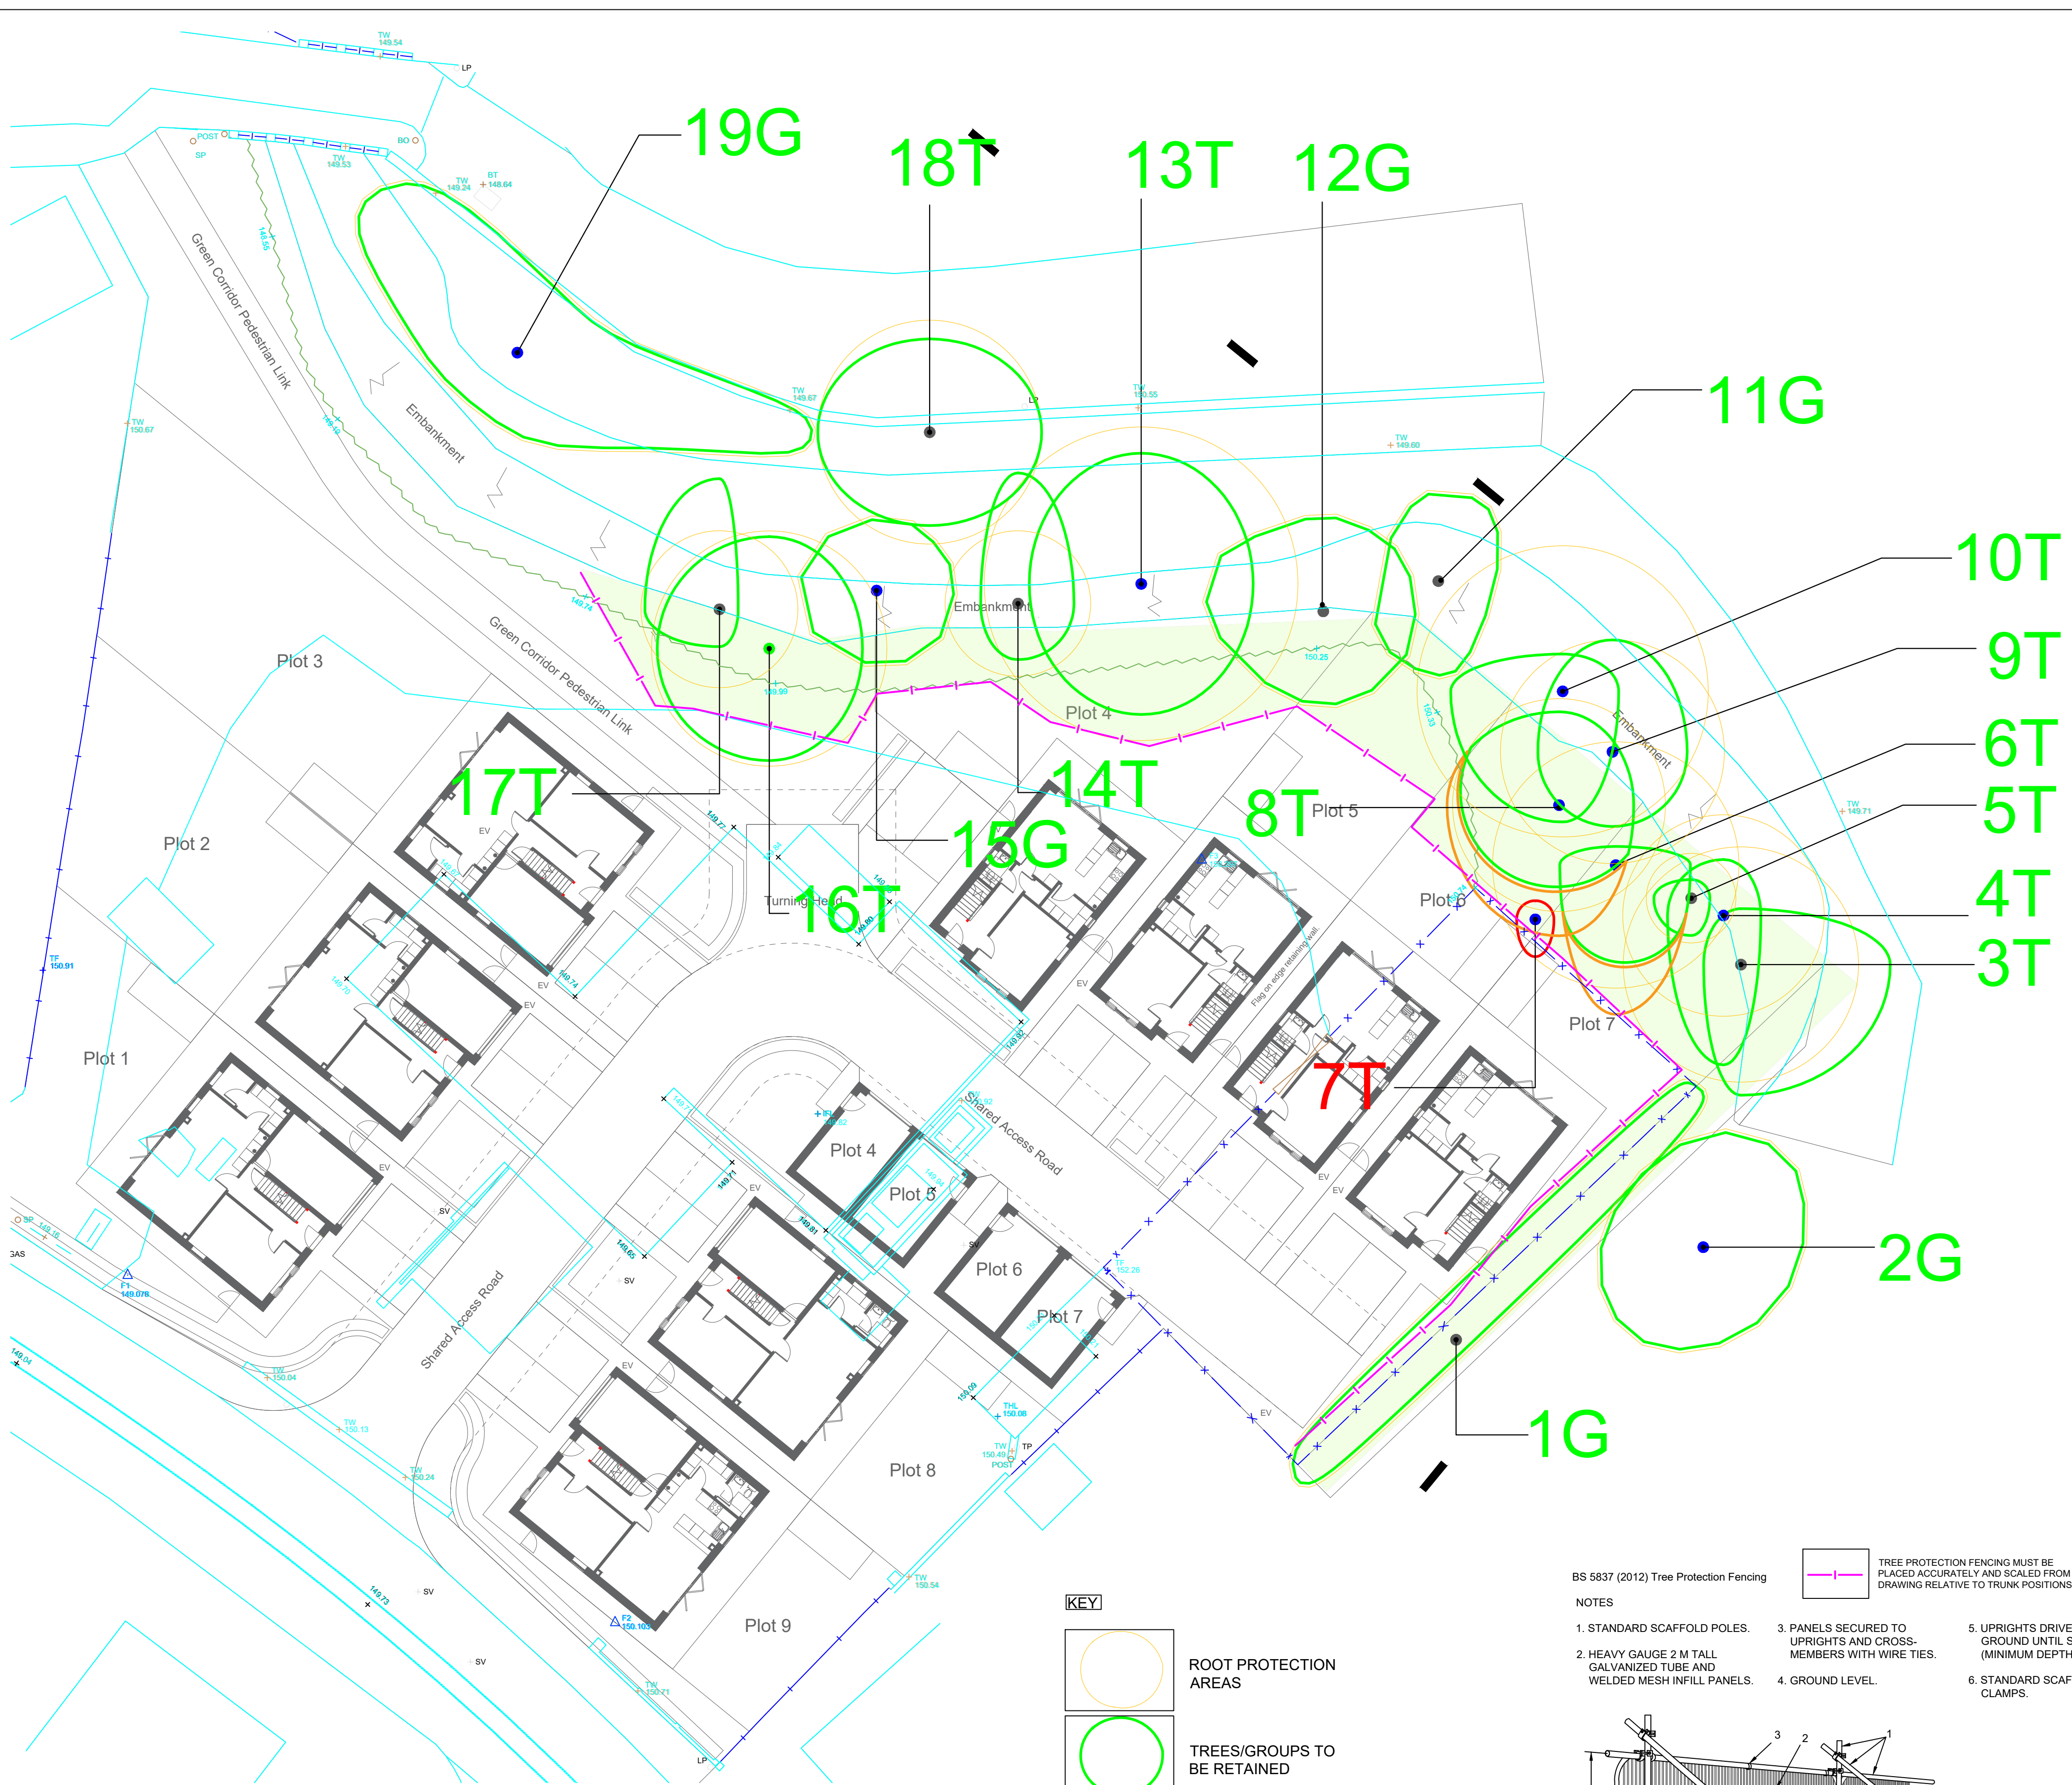
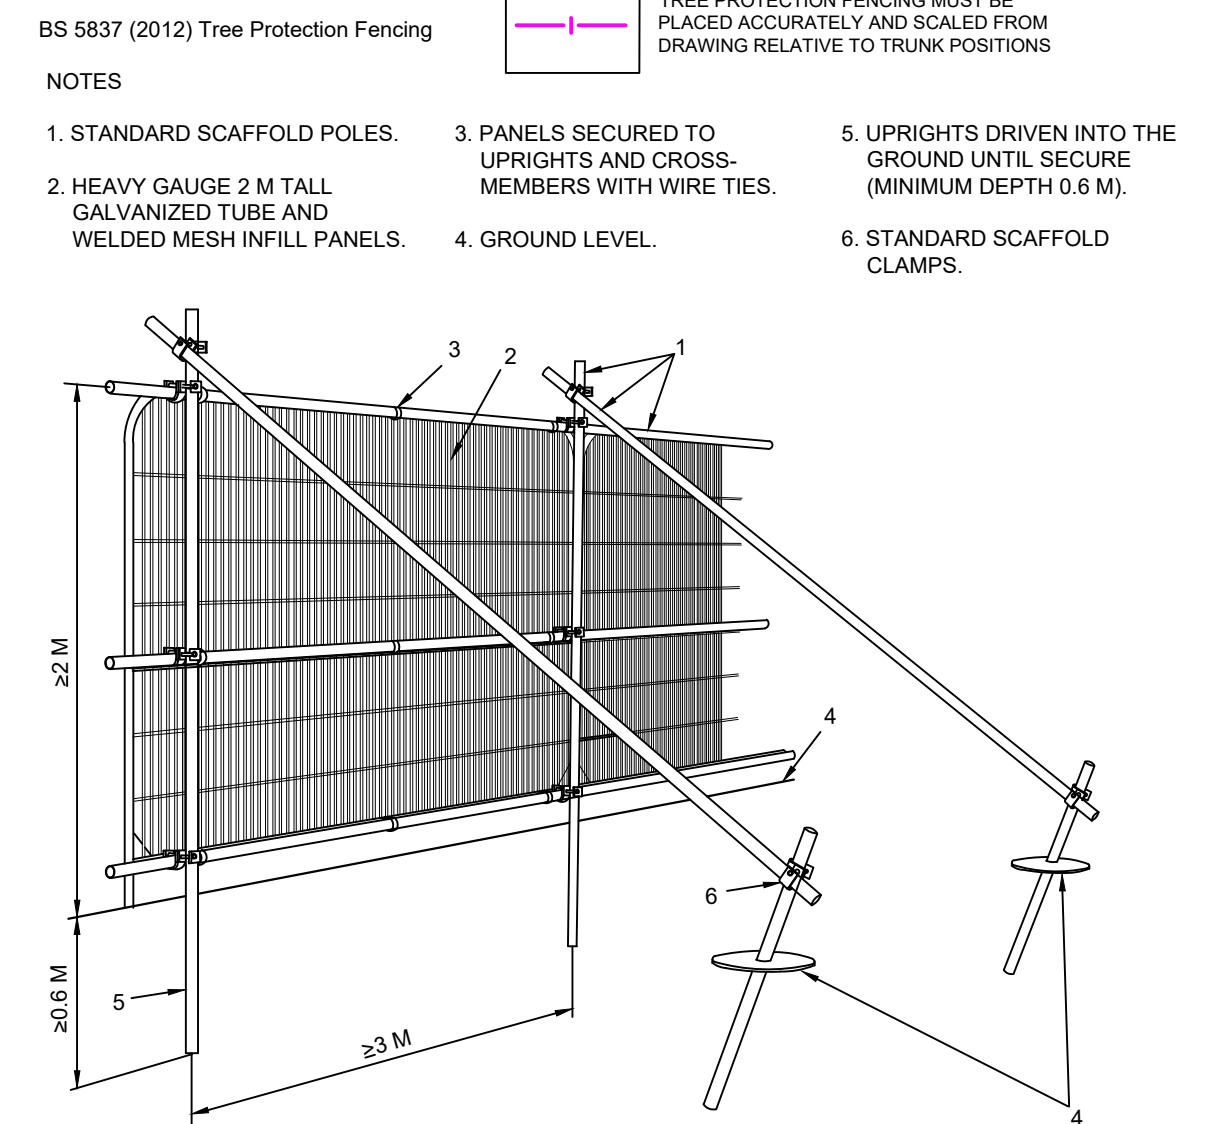


KEY

- ROOT PROTECTION AREAS
- TREES/GROUPS TO BE RETAINED
- TREES/GROUPS TO BE REMOVED
- TREE PRUNING REQUIRED
- TREE PROTECTION FENCING
- CONSTRUCTION EXCLUSION ZONES



Phase	Requirements	Method												
1 Prior to erection of protective fencing.	Undertake tree and vegetation removal and pruning works Trees/vegetation to be removed:  Trees/vegetation to be pruned: 	Refer to section 5.5 of AIA/MS report. All tree works to be carried out to BS3998: 2010, by suitably qualified and insured professional tree surgeons. The following tree felling must be undertaken at this Phase: <table border="1"><thead><tr><th colspan="2">Items requiring removal:</th></tr></thead><tbody><tr><td>7T</td><td>Lombardy Poplar</td></tr></tbody></table> The following tree pruning must be undertaken at this Phase: <table border="1"><thead><tr><th colspan="2">Items requiring pruning:</th></tr></thead><tbody><tr><td>1H</td><td>Trim the site side lateral spread as hard as possible without spoiling.</td></tr><tr><td>6T</td><td>Sycamore. Reduce the southerly lateral canopy spread by approximately 3m in length.</td></tr><tr><td>8T</td><td>Ash. Reduce the southerly lateral canopy spread by approximately 2.5m in length.</td></tr></tbody></table>	Items requiring removal:		7T	Lombardy Poplar	Items requiring pruning:		1H	Trim the site side lateral spread as hard as possible without spoiling.	6T	Sycamore. Reduce the southerly lateral canopy spread by approximately 3m in length.	8T	Ash. Reduce the southerly lateral canopy spread by approximately 2.5m in length.
Items requiring removal:														
7T	Lombardy Poplar													
Items requiring pruning:														
1H	Trim the site side lateral spread as hard as possible without spoiling.													
6T	Sycamore. Reduce the southerly lateral canopy spread by approximately 3m in length.													
8T	Ash. Reduce the southerly lateral canopy spread by approximately 2.5m in length.													
2 Prior to any construction works on site	Erection of protective fencing: To retain throughout the duration of the development: 	Protective fencing is to be erected in accordance with 5.6 of AIA/MS report. The fencing must comply with the positions shown in the Tree Protection Plan. A scale copy of the Tree Protection Plan must be used as reference and fencing positions measured from the Plan using a scale rule and/or using the provided distances where shown. No works, no storage of materials, no access, or any ground disturbance is to take place within the Tree Protection Barrier Fencing other than works specified within the Arboricultural Method Statement. Fenced areas are to be treated as Construction Exclusion Zones. Warning signs to be placed on all protective fencing. For large sections of fencing the signs must be placed at 20m intervals. Signs must be laminated and securely attached at all corners. Two signs are to be placed side by side, copies of which are attached within Appendix A.												
3 Verifying quality of protective barriers	Verify that the location and quality of tree protection barriers is adequate prior to onset of main site works.	Site visit with Arboricultural Consultant and Site Manager. Tree Officer to be pre-informed of visit. In order for set works to proceed the pro-forma in Appendix B of the AIA/MS report is to be completed and passed on to the local planning authority. If the protective barriers are not adequately, work is not to proceed until rectified.												
4 Ongoing	Maintain protective fencing	The tree protective barrier fencing is to remain in situ during all construction works.												

Phase	Requirements	Method
5	Completion of main construction and undertaking of landscaping	It is essential that ground levels within the root protection areas are not altered, either by raising or lowering soil levels, even at the landscaping stage. Landscaping operations must be undertaken in a manner that will not impact trees. Landscaping within the root protection area of trees must be undertaken in the following manner: - Any existing ground flora (grass/weeds/scrub) is to be sprayed with a systemic herbicide and left to die-off. - Dead flora is to be trimmed as hard as possible with a brush cutter or similar. The bulk of the trimmed material is to be removed by raking. - A good quality organic topsoil layer may be placed down. Small depressions may be filled (and lightly compacted underfoot). Placed topsoil soil layers must not exceed 100mm depth. - No plant machinery operating within the root protection areas to exceed 1 tonne gross weight and must only operate from properly ground protection boards such as DuraMatt Access Mats (see Appendix C). - Turf and other planting to proceed thereafter.
6	Completion of main construction and installation of boundary treatments	Within the RPAs of retained trees the wooden fencing shall be installed as follows: - Hand tools only - Exploratory post holes to be dug. Any roots encountered less than 2.5cm diameter should be cleanly cut back. - Roots in excess of 2.5cm can only be removed once arboricultural advice has been sought. - Where roots in excess of 8cm are encountered, an alternative location for the post hole is required. - Prior to the pouring of concrete a non-permeable membrane must fully line the post hole.

Tree Schedule			
Tree Number	Species	RPA Radius	Category
1G	Leyland cypress	1.8m	C3
2G	Willow, sycamore, ash and hawthorn	4.8m	B3
3T	Ash	6.3m	C2
4T	Sycamore	5.4m	B2
5T	Sycamore	2.4m	C3
6T	Sycamore	6.6m	B3
7T	Lombardy poplar	7.8m	B3
8T	Ash	5.7m	B2
9T	Sycamore	6m	B3
10T	Alder	7.8m	B3
11G	Ash x 2	4.2m	C3
12G	Ash x 2	4.2m	C3
13T	Sycamore	8.4m	B3
14T	Ash	3.9m	C3
15G	Sycamore x 1, ash x 1	5.7m	B3
16T	Sycamore	6.3m	A3
17T	Ash	4.2m	C3
18T	Ash	6m	C2
19G	Alder, ash, hawthorn, sycamore	4.5m	B3

THIS DRAWING MUST BE VIEWED IN COLOUR AND READ IN CONJUNCTION WITH ARBORICULTURAL IMPACT ASSESSMENT AND METHOD STATEMENT

No dimension to be scaled from this drawing [Date] [Dwn] [Rev]

© Copyright reserved

Landscape Architecture
Arboriculture

Trevor Bridge Associates Ltd
Ashton Old Baths
Stamford Street West
Ashton-under-Lyne
Lancs OL6 7FW

Tel: 0161-804 2099
E-mail: info@trevorbridge.co.uk

Project
Reliance Garage,
1 Turnlee Road,
Glossop

Title
TREE PROTECTION PLAN

Date	Scale(s)	Dwg no	Rev
Mar '24	1:200	7303.02	
Dwn	Chkd	@ A1	
MG			
